


I-64 EXIT 124 & ROUTE 250 DIVERGING DIAMOND INTERCHANGE (DDI) CONVERSION

Existing Configuration

Construction Phases

Phase 1	Phases 4A/4B
Phase 2	Phases 5A/5B
Phase 3	Phases 6A/6B

Construction scheduled from MAR 2021 to NOV 2022

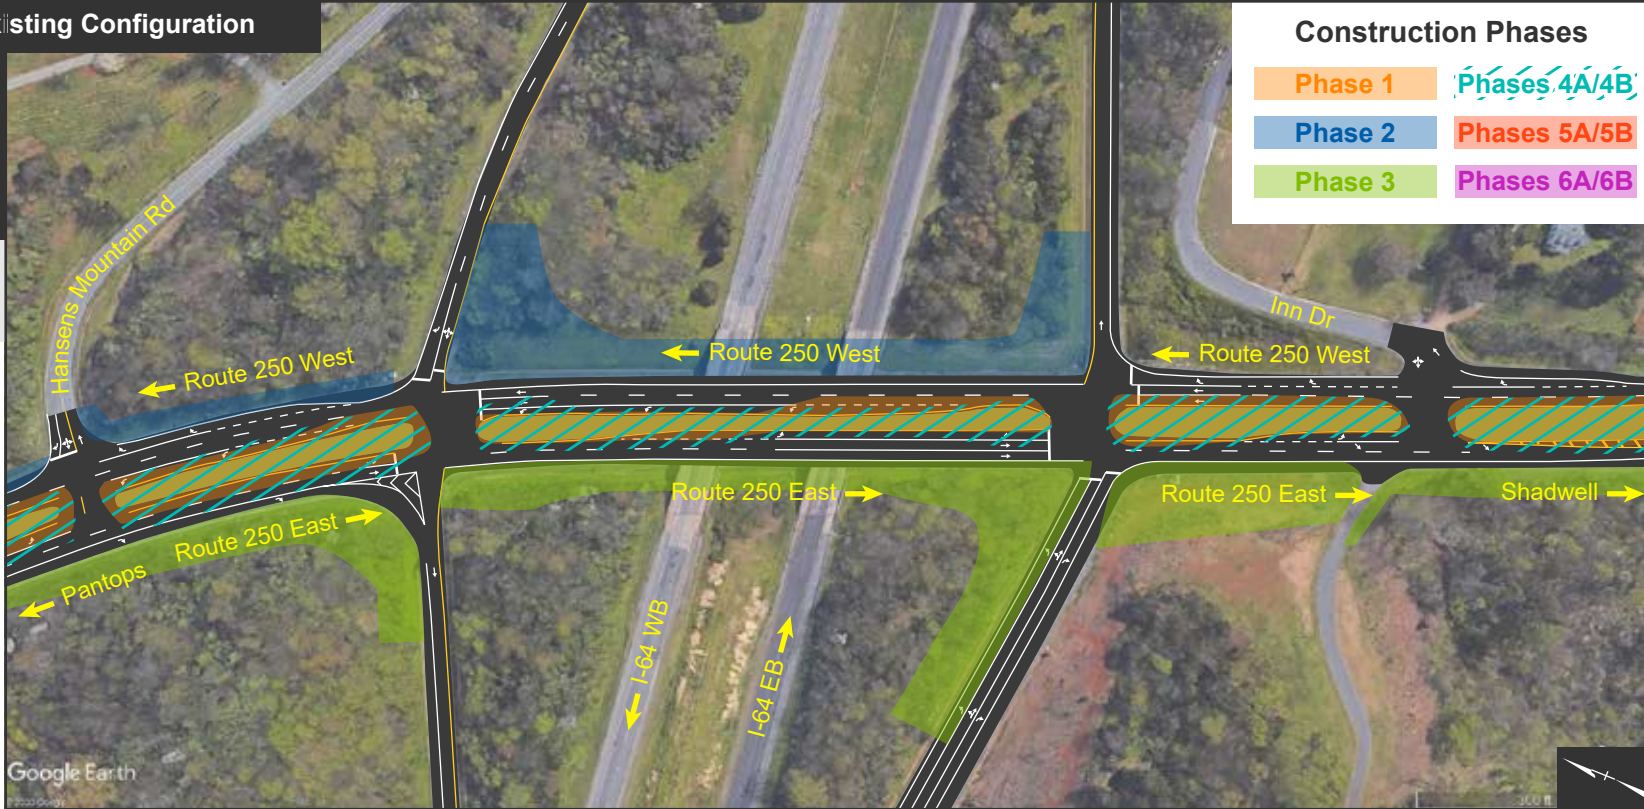

Construction Phasing Overview

Phase 1 - Mar 2021 to May 2021

Involves construction in the Rt. 250 median using non-peak single lane closures.

Phase 2 - May 2021 to June 2022

Involves construction on ramps A & D, along with the Rt. 250 WB/I-64 infield area in the shoulder area.

Phase 3 - May 2021 to July 2022

Involves construction on ramps B & C, and in the Rt. 250 EB/I-64 shoulder.

Phases 4A/4B - July 2022 to Aug 2022

Includes finalizing the medians on Rt. 250, including traffic signal installations using non-peak lane and shoulder closures.

Phases 5A/5B - Aug 2022 to Sep 2022


Involves completing the work along and channelizing the islands at Ramps A & D.

Phases 6A/6B - Sep 2022 to Oct 2022

Involves completing the work along and channelizing the islands at Ramps B & C.

Traffic switches to DDI - Aug 2022

Diverging Diamond Interchange

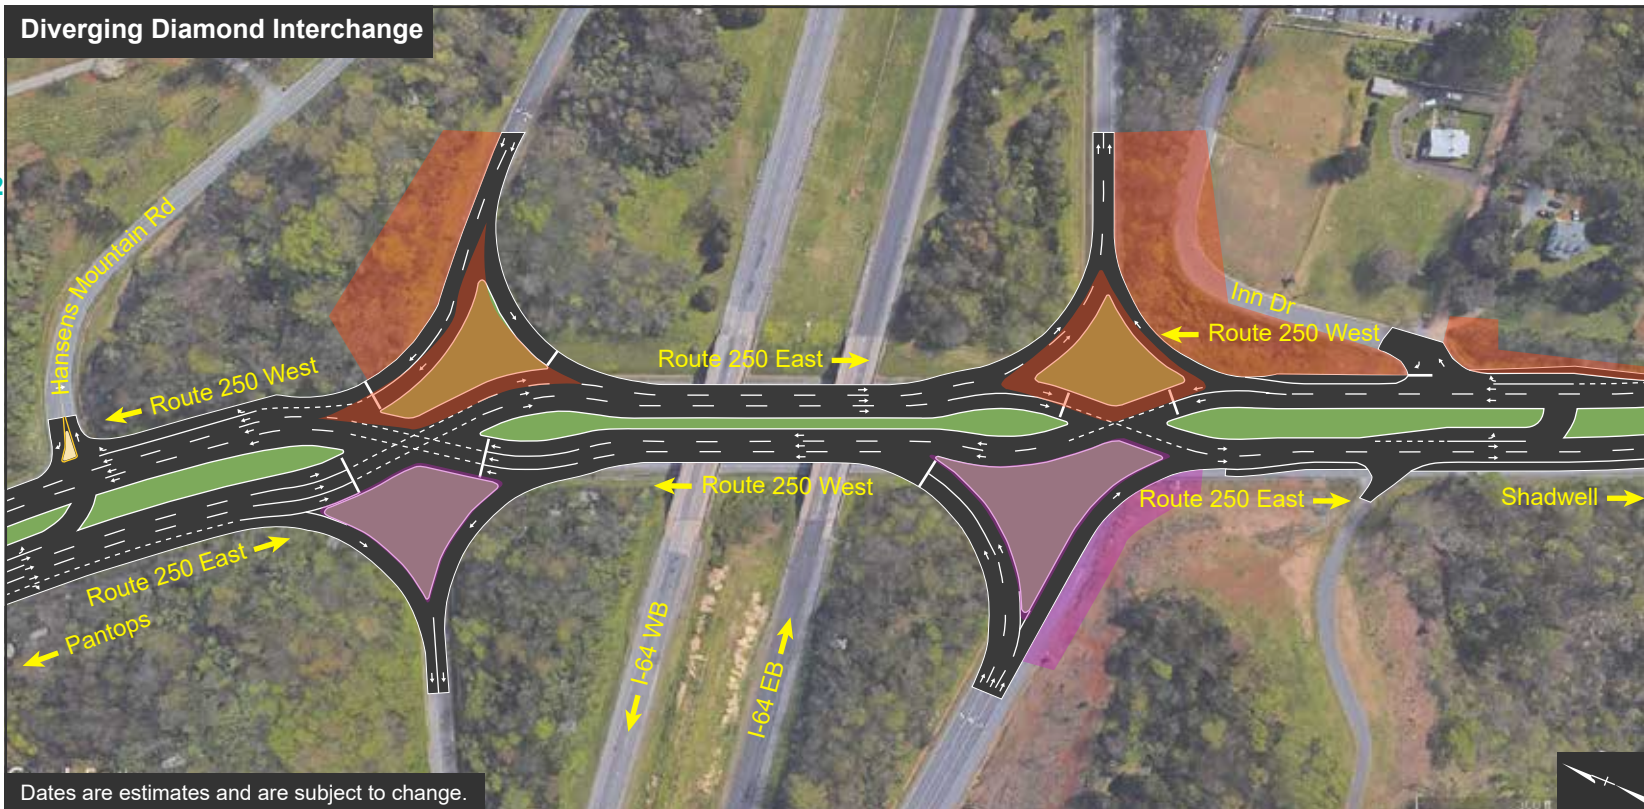

Dates are estimates and are subject to change.
